



CMA BOARD MEETING

10 SEPTEMBER 2026


PROPOSITION 68 GRANT FUNDED PROJECTS UPDATES

PROP 68 STATUS (9/10/2026)

COMPONENT 2 WELL EXTRACTION AND MEASUREMENT

Deliverable	Status
TM 2: Extraction and Measurement Demonstration Project (ET, Meter, Power)	Draft submitted to GSA in July
TM 3: Data Collection Results and Evaluation	Draft submitted to GSA in July
Well Registration and Well Metering and Reporting Plans	Drafts submitted to GSA in July
TM 1: Data Management System Updates	Draft due from Stetson in September
TM 4: Extraction and Measurement Project Implications for Basin Water Budget	Draft scheduled for submission to GSA in November
Final TMs, Outreach Materials, and Well Reporting Plans	Scheduled for submission by GSA to DWR in early December

COMPONENT 2
WELL EXTRACTION AND MEASUREMENT

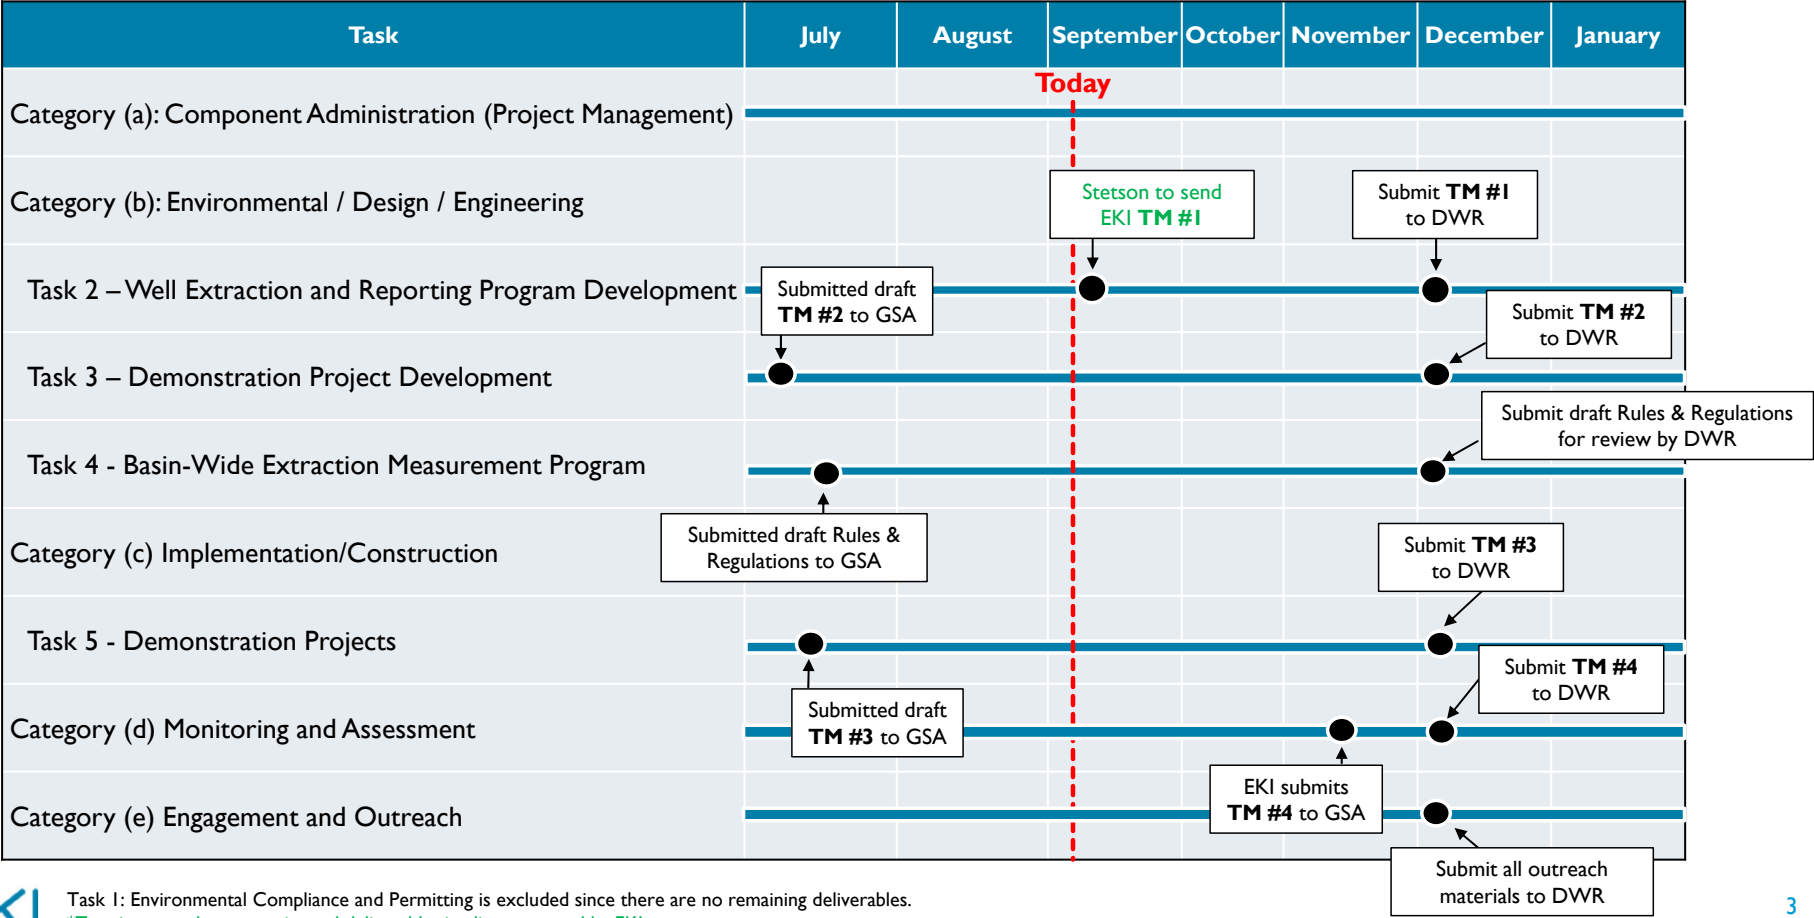


Task 1: Environmental Compliance and Permitting is excluded since there are no remaining deliverables.
*Text in green denotes estimated deliverable timelines assumed by EKI

PROP 68 STATUS (9/10/2026)

COMPONENT 5 MONITORING IMPROVEMENT AND EXPANSION

Deliverable	Status
Geosyntec monitoring well design plans and permits	Completed in July
Stream gage installation	Scheduled for completion in September
TM: Stream Gage Installation	Draft scheduled for submission to GSA in October
TM: Groundwater Dependent Ecosystem Verification	Draft scheduled for submission to GSA in October
Monitoring well installation	Scheduled for November
Final TMs and Outreach Materials	Scheduled for submission by GSA to DWR in early-mid December

COMPONENT 5
MONITORING IMPROVEMENT AND EXPANSION

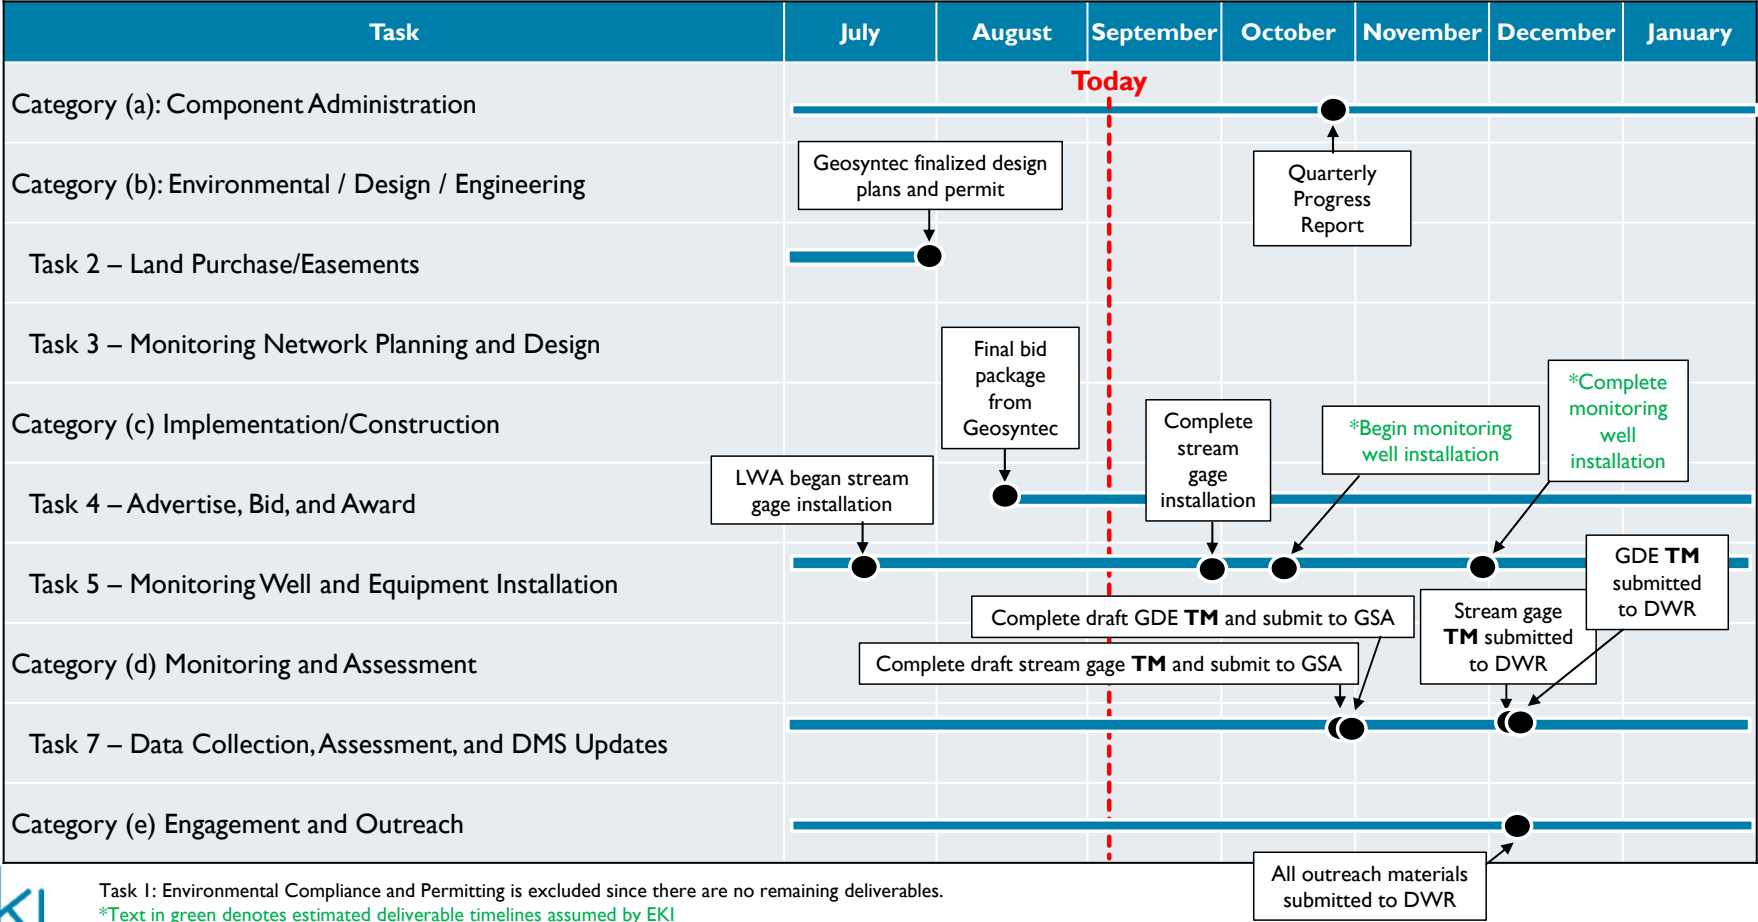

Task 1: Environmental Compliance and Permitting is excluded since there are no remaining deliverables.

*Text in green denotes estimated deliverable timelines assumed by EKI

QUESTIONS?
